

PROJECT ORIENTATION

Government Procurement Digital Platform

How we take the Government Procurement platform from kickoff to a live website in two weeks, and the complete platform in six.

CLIENT

Mohamed Ibn Fayez Kheir

DELIVERY LEAD

Ayna Sulaiman


KICKOFF

Monday 13 July 2026

01 · ROADMAP

The roadmap.

Value ships early. Each phase stands alone, and each is built knowing what comes next.

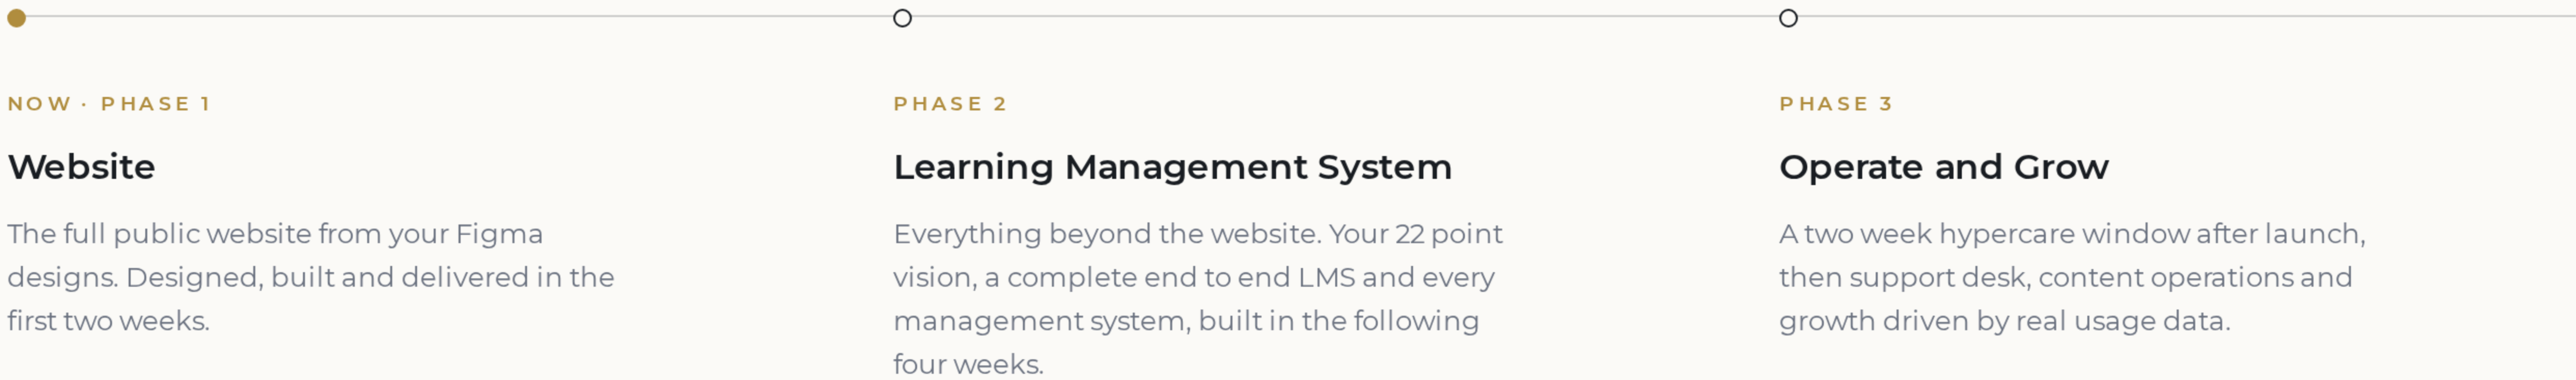

Every Phase 1 decision is made with the end state in view. Nothing is rework waiting to happen.

02 · SCOPE · PHASE 1

Phase 1 scope. The website.

Every screen in your designs and every page in the navigation. Desktop first, built to your Figma and delivered in the first two weeks.

SCREENS AND PAGES

01	Home, Win Contracts view (audience toggle)
03	Advisory Services, Win Contracts
05	Our Expertise, founder profile and credentials
07	Courses and resources listing (courses, artefacts, bundles) with filters, levels and pricing
09	Explore Tender Websites, Global (search, country filter, featured list)
11	Forum home (search, recent answers, categories, featured questions)
13	Forum answer page
15	Contact Us (form, phone, WhatsApp, email, address)
17	Navigation, breadcrumbs, footer and 404

02	Home, Award Contracts view
04	Advisory Services, Award Contracts
06	Insights, articles with topics, sorting and featured stories
08	Course page with preview video, outcomes, description and price panel
10	Explore Tender Websites, Australia
12	Forum category view
14	Submit a Question
16	Privacy Policy and Terms of Use
18	Book a Consultation flow into Contact Us

Every dynamic area above (tenders, forum, insights, courses) is powered by the management systems delivered in Phase 2.

03 · SCOPE · PHASE 2

Phase 2 scope. The learning platform.

Your 22 point brief answered in full, a complete end to end LMS, and the management systems behind every dynamic screen. Delivered in the four weeks after the website.

THE 22 POINT BRIEF

01	Privacy Act 1988 and APP compliant data handling	02	Penetration testing with shareable summaries
03	Secure video streaming, no easy download or copy	04	Text lessons and downloadable resources
05	Transcripts synced to the video	06	Courses, modules and lessons
07	Programs with program certificates	08	Access restricted to enrolled students
09	Free preview lessons	10	One off purchases and memberships
11	Auto marked quizzes and assessments	12	Progress and completion tracking
13	Fully customisable certificates	14	Bulk enrolment for organisations
15	Q&A and discussion linked to courses	16	Self service teacher and admin interfaces
17	Single sign on with the website	18	Stripe payments, automatic GST, AU or UAE entity
19	Native email and CRM	20	Live online teaching sessions
21	Affiliate and referral program	22	Embedded AI course coach

This is the total scope. The website ships first, the platform follows, and nothing gets built twice.

A COMPLETE LMS, END TO END

+	Student dashboard and profiles	+	Learning paths and prerequisites
+	Drip content scheduling	+	Notes and bookmarks
+	Reviews and ratings	+	Email and in app notifications
+	Coupons and promotions	+	Reporting and analytics dashboards
+	Badges and gamification	+	Multi instructor management


DYNAMIC CONTENT, MANAGED

◆	Tender directory manager	◆	Forum moderation and publishing
◆	Insights publishing studio	◆	Courses, artefacts and bundles catalogue
◆	Pricing and bundle control	◆	Services and homepage content
◆	Contact enquiries inbox	◆	Navigation, footer and site settings

04 · TIMELINE

Delivery timeline.

Eight weeks end to end. The website live in two, the full platform in six, and a two week hypercare window after launch.

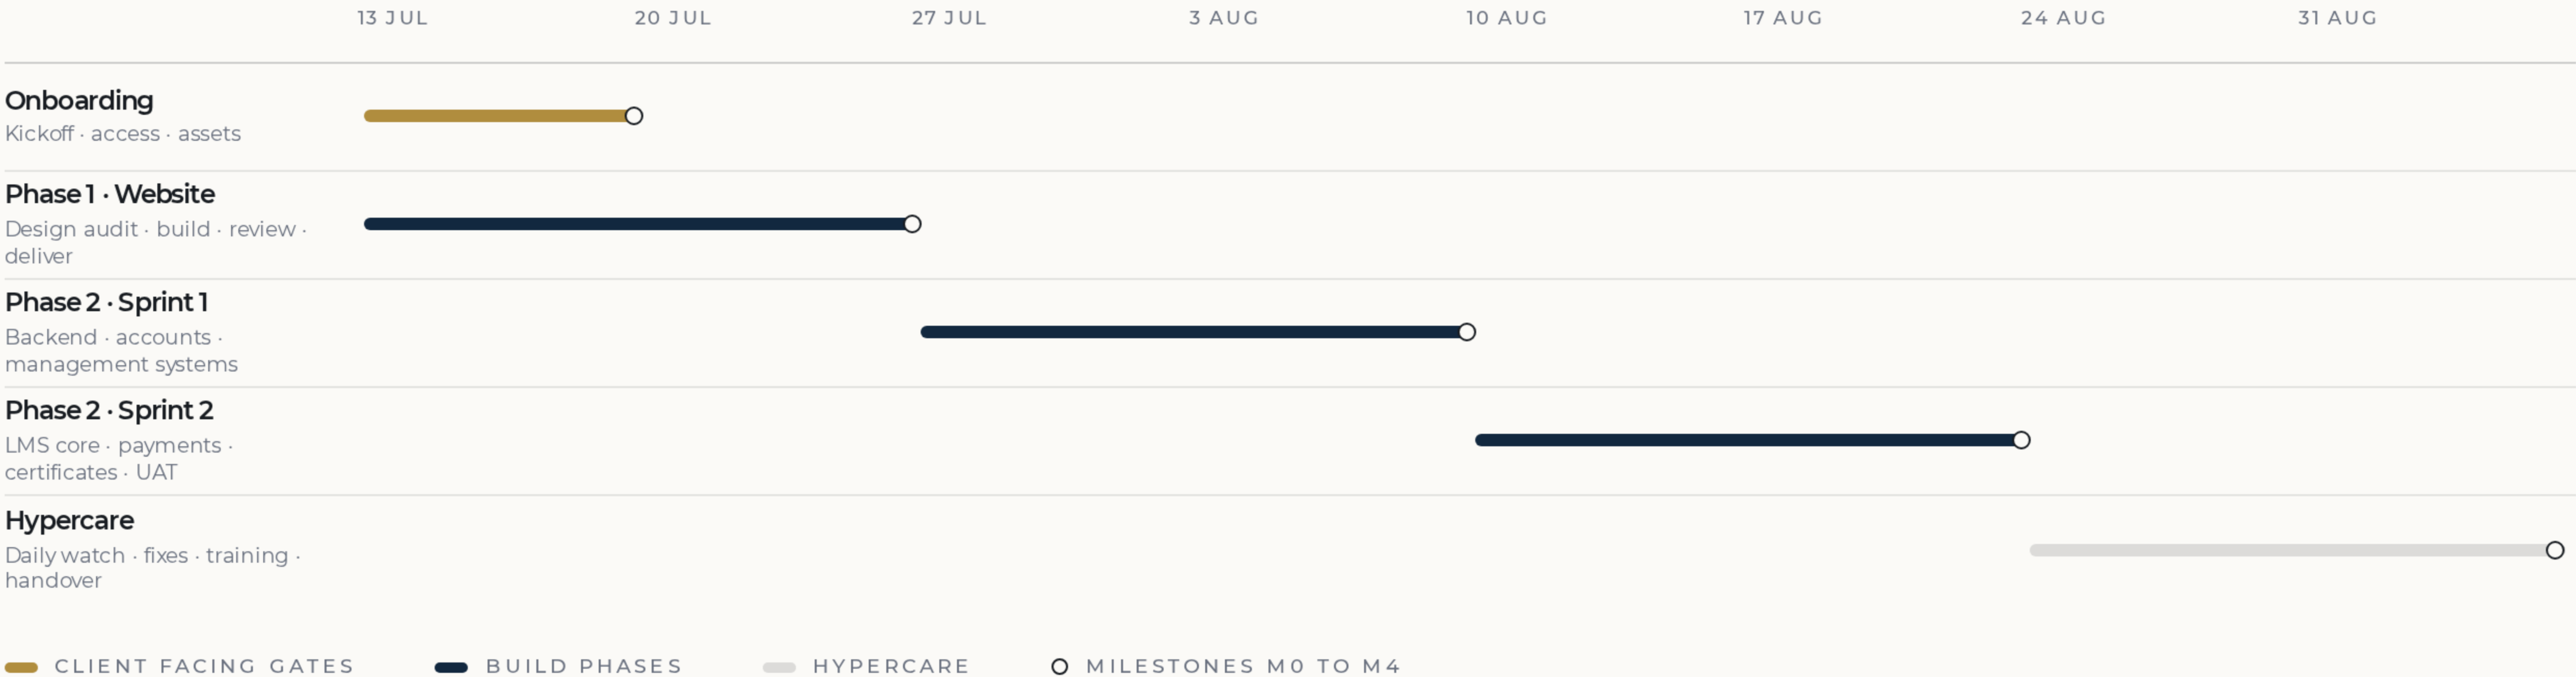

05 · PLAN

Phase plan.

Progress is shown as working software, never as status slides. Every Friday you see it live on the staging site.

PHASE 1 · 13 TO 24 JUL	Website design, build and delivery	Every screen from your Figma designed, built and reviewed, then delivered live on your domain at the end of week two.
PHASE 2 · 27 JUL TO 7 AUG	Backend and management systems	Accounts and admin, tender directory manager, forum moderation and publishing, insights studio, courses and pricing catalogue, contact inbox and site settings.
PHASE 2 · 10 TO 21 AUG	Learning platform	Enrolment and payments with GST, lessons and secure video, quizzes, progress and certificates, plus acceptance testing and launch.
HYPERCARE · 24 AUG TO 4 SEP	Watch, fix, train and hand over	Daily monitoring with priority fixes, training sessions for your team, and full handover of credentials and documentation.

M0 13 JUL Onboarded	M1 24 JUL Website delivered	M2 7 AUG Progress demo	M3 21 AUG Platform live	M4 4 SEP Handover
---------------------------	-----------------------------------	------------------------------	-------------------------------	-------------------------

06 · TEAM

The team.

Everything routes through one relationship: you and Ayna. You never chase anyone.

Zain Sheikh FOUNDER & CEO Senior accountability. Commercially responsible, and personally reachable if anything needs escalating.	Ayna Sulaiman PROJECT MANAGER Your single point of contact, every day. Runs the plan, the reporting, the risks, and the standard you experience.	Bushra DEVELOPER Builds what you will touch daily. The public pages, the admin systems, and the integrations behind them.	Sohaib TECHNICAL LEAD Architecture and engineering standards. The forward compatible decisions carry his signature.	Zainab QA AND TESTING Quality gatekeeper. Tests every screen, every browser and every workflow before you ever see it.
---	--	---	---	--

Engineers are never client facing without the PM present, so context never fragments and nothing gets promised twice.

07 · COMPLIANCE

Security and **compliance.**

Student and business data is handled in line with Australian law and recognised international standards, from the first line of code.

AUSTRALIA	Privacy Act 1988 and the APPs	All personal data is collected minimally, stored securely and handled in line with the Australian Privacy Principles, with consent captured at every collection point.
SECURITY	ISO 27001 and SOC 2 aligned	Security practice aligned to relevant international standards where they apply, with regular penetration testing and a summary we can share.
INTERNATIONAL	GDPR where it applies	Consent, cookie controls and data subject rights honoured for international students and visitors.
CONTENT	Secure video streaming	Course video is streamed through protected, expiring links that prevent easy downloading or copying of your content.

Compliance is designed in from day one, not added later.

08 · WAYS OF WORKING

Ways of **working.**

RITUAL	WHEN	WHAT YOU GET
Written report	Friday	A written summary of what is done, what comes next, any blockers and the decisions we need from you.
Client call	Tuesday, 30 min	Open decisions are resolved together and the minutes reach you within two hours.
Friday demo	Every Friday	You see working software on the staging site and you try it yourself.
WhatsApp	Any time	We reply within four business hours and confirm anything material by email.

Notion holds the ledger, Jira runs the build, and a ClickUp support desk opens the day we go live.

- 01 **Demo or it is not done.** Progress appears on staging, never in a status slide.
- 02 **The paper trail.** WhatsApp agreements are confirmed in writing the same day, or they did not happen.
- 03 **No surprises.** You hear about risk from us before you feel it.
- 04 **Visible trades.** New scope is exchanged, never silently absorbed into the timeline.
- 05 **Zero defect gates.** No serious defect stays open past any milestone. If you felt it, we triage it.

NEXT

Kickoff. Monday 13 July.

Forty five minutes: scope walkthrough, your Figma tour, the mobile decision, the asset checklist. Summary in your inbox within two hours.

72 HOURS	Everything stood up	Access verified, tooling live, and the Phase 1 build underway.
WEEK ONE	Visible momentum	A staging URL with your pages taking shape. Proof before promises.
TWO WEEKS	Website delivered	Every screen from your designs, live on your domain by 24 July.
SIX WEEKS	Platform live	The complete learning platform delivered by 21 August, with a two week hypercare window to follow.
